COLLISION_REPORT · comprobación sistemática entre familias

Vóxeles de 0,20 m. Se distingue el contacto intencionado (apoyo, anclaje, plantación) de la interpenetración accidental.

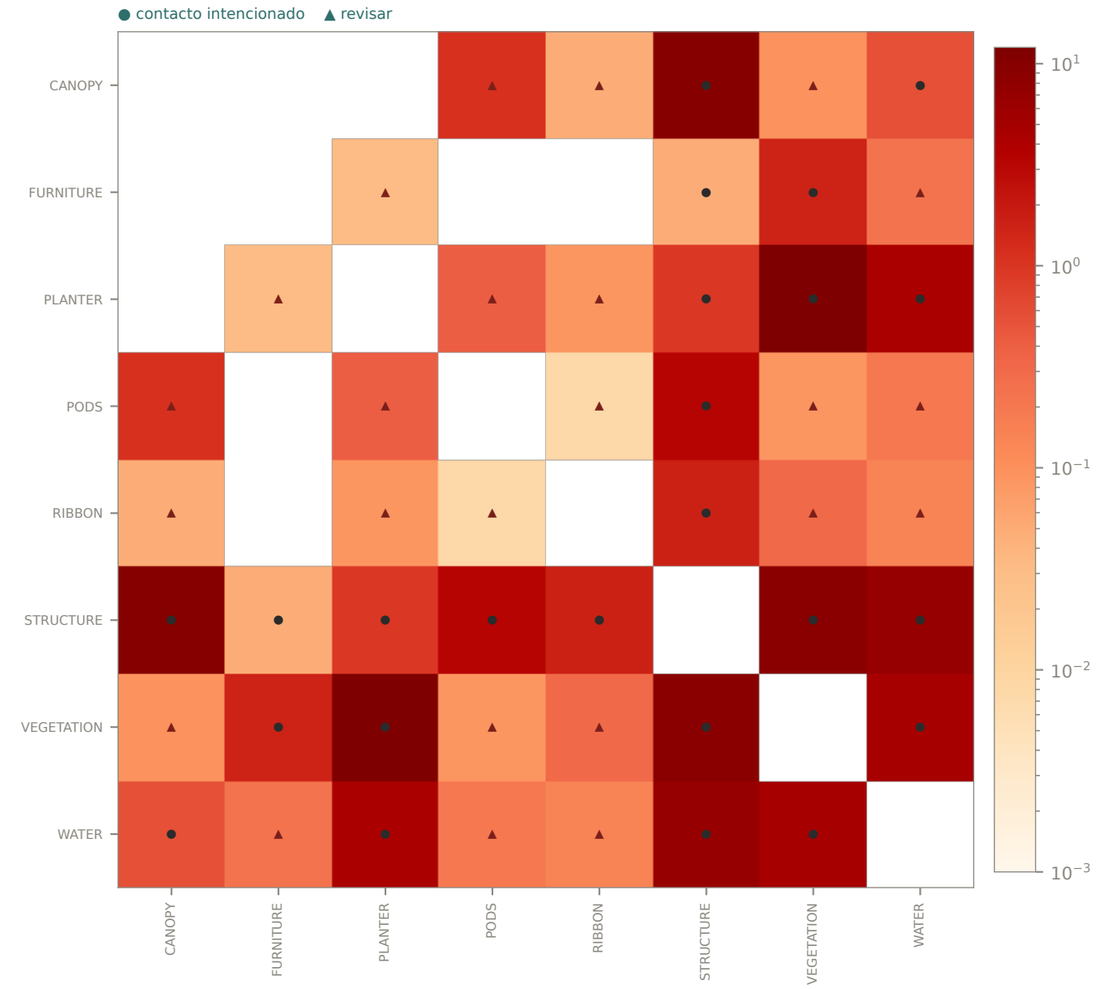

familia A	familia B	vóxeles	m³	lectura
PLANTER	VEGETATION	1505	12.04	intencionado
CANOPY	STRUCTURE	1235	9.88	intencionado
STRUCTURE	VEGETATION	1148	9.18	intencionado
STRUCTURE	WATER	857	6.86	intencionado
VEGETATION	WATER	583	4.66	intencionado
PLANTER	WATER	546	4.37	intencionado
PODS	STRUCTURE	413	3.30	intencionado
RIBBON	STRUCTURE	200	1.60	intencionado
FURNITURE	VEGETATION	198	1.58	intencionado
CANOPY	PODS	143	1.14	REVISAR
PLANTER	STRUCTURE	124	0.99	intencionado
CANOPY	WATER	71	0.57	intencionado
PLANTER	PODS	50	0.40	REVISAR
RIBBON	VEGETATION	39	0.31	REVISAR
FURNITURE	WATER	29	0.23	REVISAR
PODS	WATER	25	0.20	REVISAR
RIBBON	WATER	18	0.14	REVISAR
CANOPY	VEGETATION	12	0.10	REVISAR
PLANTER	RIBBON	11	0.09	REVISAR
PODS	VEGETATION	11	0.09	REVISAR
CANOPY	RIBBON	6	0.05	REVISAR
FURNITURE	STRUCTURE	6	0.05	intencionado
FURNITURE	PLANTER	4	0.03	REVISAR
PODS	RIBBON	1	0.01	REVISAR

CONTACTOS INTENCIONADOS reconocidos: mástil↔disco (anclaje), estructura↔cinta (apoyo), jardinera↔vegetación (plantación), estructura↔agua (bajantes y aros de balsa), estructura↔cápsula (cunas y pies). El resto se marca para revisión.

par	objeto A	objeto B	x,y,z	vóx	m³
RIBBON×VEGETATION	RIBBON_DECK	VEG2_COLGANTE	80,3,5.8	6	0.048
CANOPY×VEGETATION	LEAF_M2	VEG2_ARBOL_A	21,31,4.3	6	0.048
PLANTER×RIBBON	MAST_2	RIB_SUP	-62,23,0.3	6	0.048
RIBBON×VEGETATION	RIB_SUP	VEG2_TREPADORA	-62,23,2.9	5	0.040
RIBBON×VEGETATION	RIBBON_DECK	VEG2_COLGANTE	14,30,5.8	5	0.040
PODS×WATER	POD_M	MAIN	-63,14,0.4	5	0.040
CANOPY×VEGETATION	LEAF_M2	VEG2_ARBOL_A	21,31,4.5	5	0.040
PODS×VEGETATION	POD_TRAIN	VEG2_TROPICAL	-80,-6,1.4	5	0.040
RIBBON×VEGETATION	RIBBON_DECK	VEG2_COLGANTE	-82,-6,5.8	4	0.032
RIBBON×VEGETATION	RIBBON_DECK	VEG2_COLGANTE	-60,-11,5.8	4	0.032
RIBBON×VEGETATION	RIBBON_DECK	VEG2_COLGANTE	-59,-11,5.8	4	0.032
RIBBON×VEGETATION	RIBBON_DECK	VEG2_COLGANTE	14,29,5.8	4	0.032
PODS×WATER	POD_M	MAIN	-64,16,0.2	4	0.032
RIBBON×VEGETATION	RIBBON_DECK	VEG2_COLGANTE	-82,-5,5.8	3	0.024
RIBBON×VEGETATION	RIBBON_DECK	VEG2_COLGANTE	80,4,5.8	3	0.024
PODS×WATER	POD_M	MAIN	-64,16,0.1	3	0.024
PODS×WATER	POD_M	MAIN	-62,15,0.1	3	0.024
PODS×WATER	POD_S	NEB_POST	-61,19,1.4	3	0.024
PODS×WATER	POD_M	NEB_POST	68,15,1.9	3	0.024
PODS×WATER	POD_M	NEB_POST	68,15,1.9	3	0.024
RIBBON×WATER	RIBBON_RAIL	TKPOLE	-72,17,7.0	3	0.024
