COLLISION_REPORT Â· comprobaciÃ³n sistemÃ¡tica entre familias

VÃ³xeles de 0,20 m. Se distingue el contacto intencionado (apoyo, anclaje, plantaciÃ³n) de la interpenetraciÃ³n accidental.

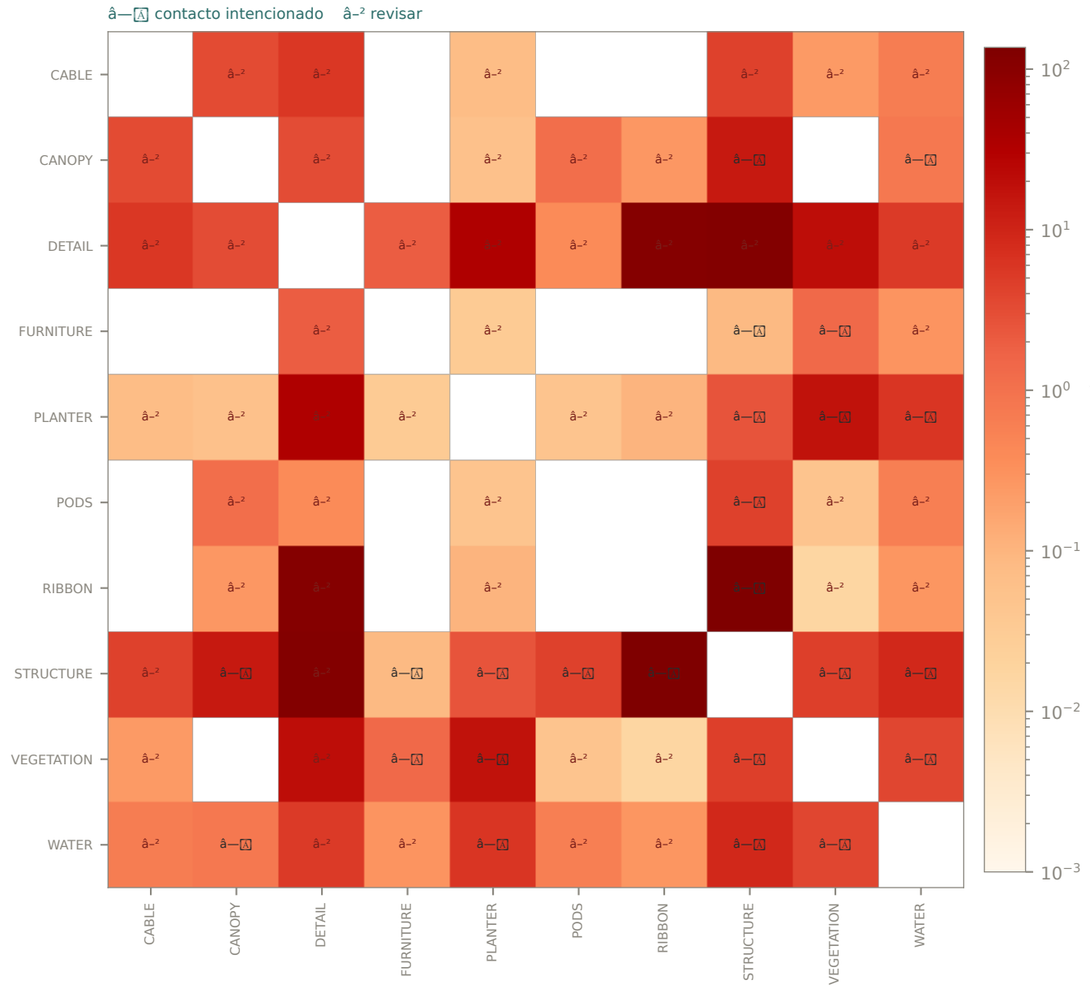

familia A	familia B	vÃ³xeles	mÂ³	lectura
RIBBON	STRUCTURE	17059	136.47	intencionado
DETAIL	STRUCTURE	14762	118.10	REVISAR
DETAIL	RIBBON	14088	112.70	REVISAR
DETAIL	PLANTER	4158	33.26	REVISAR
DETAIL	VEGETATION	2457	19.66	REVISAR
PLANTER	VEGETATION	2233	17.86	intencionado
CANOPY	STRUCTURE	1718	13.74	intencionado
STRUCTURE	WATER	1077	8.62	intencionado
PLANTER	WATER	751	6.01	intencionado
CABLE	DETAIL	707	5.66	REVISAR
DETAIL	WATER	667	5.34	REVISAR
STRUCTURE	VEGETATION	564	4.51	intencionado
CABLE	STRUCTURE	557	4.46	REVISAR
PODS	STRUCTURE	540	4.32	intencionado
VEGETATION	WATER	473	3.78	intencionado
CABLE	CANOPY	423	3.38	REVISAR
CANOPY	DETAIL	389	3.11	REVISAR
PLANTER	STRUCTURE	311	2.49	intencionado
DETAIL	FURNITURE	244	1.95	REVISAR
FURNITURE	VEGETATION	174	1.39	intencionado
CANOPY	PODS	142	1.14	REVISAR
CANOPY	WATER	100	0.80	intencionado
CABLE	WATER	81	0.65	REVISAR
PODS	WATER	76	0.61	REVISAR
DETAIL	PODS	50	0.40	REVISAR
FURNITURE	WATER	36	0.29	REVISAR

CONTACTOS INTENCIONADOS reconocidos: mÃ¡stilâ†”diana (anclaje), estructuraâ†”cinta (apoyo), jardineraâ†”vegetaciÃ³n (plantaciÃ³n), estructuraâ†”agua (bajantes y aros de balsa), estructuraâ†”cÃ¡psula (cunas y pies). El resto se marca para revisiÃ³n.

par	objeto A	objeto B	x,y,z	vÃ³xeles	mÂ³
DETAILÃ—RIBBON	LIFT_TOWER	RIBBON_DECK	-69,4,6.0	6	0.048
DETAILÃ—VEGETATION	ATRIO_BOLARDO	VEGA_HELECHO_M_B	55,2,0.7	6	0.048
DETAILÃ—WATER	DECK_JUNTAS	BASIN_B-C1a	-56,9,6.0	6	0.048
CABLEÃ—STRUCTURE	LCBL	PRIMARY_C2-L2	18,5,8.9	6	0.048
CABLEÃ—STRUCTURE	LCBL	SAT_C3-L2	62,-2,8.2	6	0.048
RIBBONÃ—WATER	RIBBON_DECK	BASIN_B-C1a	-56,9,6.0	6	0.048
DETAILÃ—STRUCTURE	LIFT_TOWER	PRIMARY_C1-L2	-69,3,7.8	5	0.040
DETAILÃ—STRUCTURE	DECK_CANALETA	MAST_3	-50,26,6.0	5	0.040
DETAILÃ—STRUCTURE	DECK_CANALETA	MAST_3	-50,26,6.0	5	0.040
DETAILÃ—RIBBON	LIFT_TOWER	RIBBON_DECK	-69,4,6.0	5	0.040
DETAILÃ—RIBBON	LIFT_TOWER	RIBBON_RAIL	-69,4,6.1	5	0.040
DETAILÃ—RIBBON	LIFT_TOWER	RIBBON_RAIL	-69,4,7.1	5	0.040
DETAILÃ—PLANTER	ATRIO_BOLARDO	MAST_2	55,2,0.3	5	0.040
DETAILÃ—VEGETATION	BENCH_CANTO_1_0	VEGA_ALOCASIA_H_	2,6,0.4	5	0.040
DETAILÃ—VEGETATION	ATRIO_BOLARDO	VEGA_HELECHO_M	59,2,0.7	5	0.040
CABLEÃ—STRUCTURE	LCBL	SAT_C2-L2	7,22,8.7	5	0.040
CABLEÃ—STRUCTURE	LCBL	NODE	43,-1,9.9	5	0.040
CABLEÃ—STRUCTURE	LCBL	SAT_C3-L2	61,-0,8.2	5	0.040
CABLEÃ—STRUCTURE	LCBL	PRIMARY_C3-L2	60,-3,8.5	5	0.040
CANOPYÃ—DETAIL	LEAF_OV	LIFT_TOWER	5,32,8.0	5	0.040
CANOPYÃ—DETAIL	LEAF_M1	STAIR_SB	67,-6,4.5	5	0.040
